

**BLACKFEET COMMUNITY WATER PROJECT  
BCWP P1-001 - Intake  
Stoddard Construction, Contractor**

February 25, 2003




02/20 Preparing to pour thrust blocks & supports for discharge manifold.




6 CU yds of concrete in place-DIP wrapped, snowing and warm today, area covered to protect after pour.



2/24 snow and cold, equipment won't start.

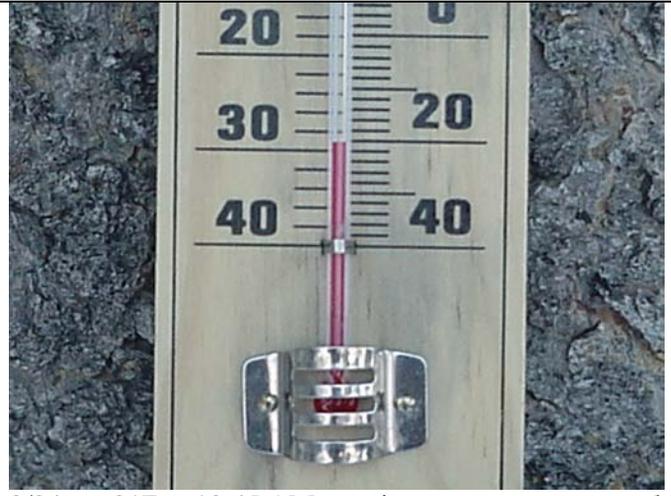

2/24 -21F at 10:45 AM, starting to warm up, no work today.

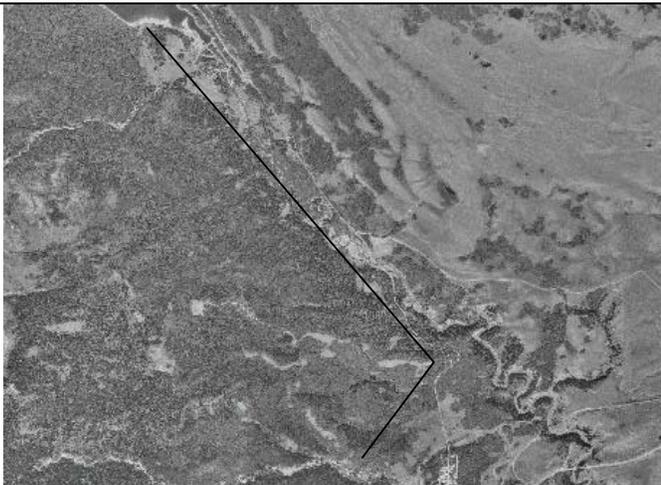

Sat. Photo of area, lake upper left and ↑-East Glacier. The line represents approx location of pipeline.

Contractor has been able to install discharge manifold and cover. All activity at site will stop on March 1. This is in accordance with mitigation measures developed to protect the grizzly and their young. This period may continue through July 15.

Site restoration, intake screen and other remaining items in the contract will be carried out as planned in the early summer.

Sat. photo at left provides overview of work area. Intake structure at the lakeshore and the approx. 20,000 of pipeline that was installed.

While there is a lot of work remaining to do, much has been accomplished. The efforts of the project engineers, design engineers, contractor, the ongoing support of funding agencies and our staff are greatly appreciated.
